

Project Planning Phase
Project Planning Template (Product Backlog, Sprint Planning, Stories, Story points)

Date	01 November 2025
Team ID	NM2025TMID08851
Project Name	Laptop Request Catalog Item
Maximum Marks	5 Marks

Product Backlog, Sprint Schedule, and Estimation:

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-1	Foundation & Data Structure	USN-1	Governance Setup: Initiate project traceability by establishing and activating the "Laptop Request" Local Update Set to capture all configuration elements.	1	High	Prabhaharan D
		USN-2	Catalog Item Creation: Build the fundamental Service Catalog item , title it "Laptop Request," and classify it under the Hardware category for user accessibility.	2	High	Vishnukumar S
		USN-3	Variable Definition: Implement the foundational data collection framework by defining the four core variables (laptop_model, justification, additional_accessories, accessories_details) on the catalog form.	3	High	Pavankanth V and Mohammed Arsath K

Sprint-2	Dynamic Form Logic	USN-4	Dynamic Policy Implementation: Develop the necessary Catalog UI Policy logic to control visibility and mandatory status of the 'Accessories Details' field based on the 'Additional Accessories' checkbox selection.	5	High	Vishnukumar S
		USN-5	UX Reset Action: Implement the client-side ' Reset Form ' UI Action on the sc_cart table to provide users with a rapid method to clear all input fields and restart the request.	3	Medium	Prem Kumar M V
Sprint-3	Deployment & Validation	USN-6	Deployment Preparation: Finalize the artifact for migration by marking the Update Set as Complete and exporting the solution package to an XML file.	1	High	Vishnukumar S
		USN-7	Functional Testing: Execute end-to-end validation, including verification of dynamic form behavior, mandatory field enforcement, and the correct function of the 'Reset Form' client script.	4	High	Prabhakaran D

Project Tracker, Velocity & Burndown Chart:

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed (Actual)	Sprint Release Date (Actual)
Sprint-1	6	1 Day	25 Oct 2025	25 Oct 2025	6	25 Oct 2025
Sprint-2	8	1 Day	26 Oct 2025	26 Oct 2025	8	26 Oct 2025
Sprint-3	5	1 Day	27 Oct 2025	27 Oct 2025	5	27 Oct 2025
Total	19	3 days			19	


Velocity:

$Average\ Velocity = \frac{Total\ Story\ Points\ Completed}{Total\ Duration\ in\ Days}$

Total: 19 points over 3 days → **Velocity** = 6.33 points/day

Burndown Chart:

A burn down chart is a graphical representation of work left to do versus time. It is a critical Agile metric used to track whether the development team is on pace to complete the entire backlog (19 points) within the allocated timeframe (3 days). The chart compares the ideal, linear reduction of work against the actual daily progress.

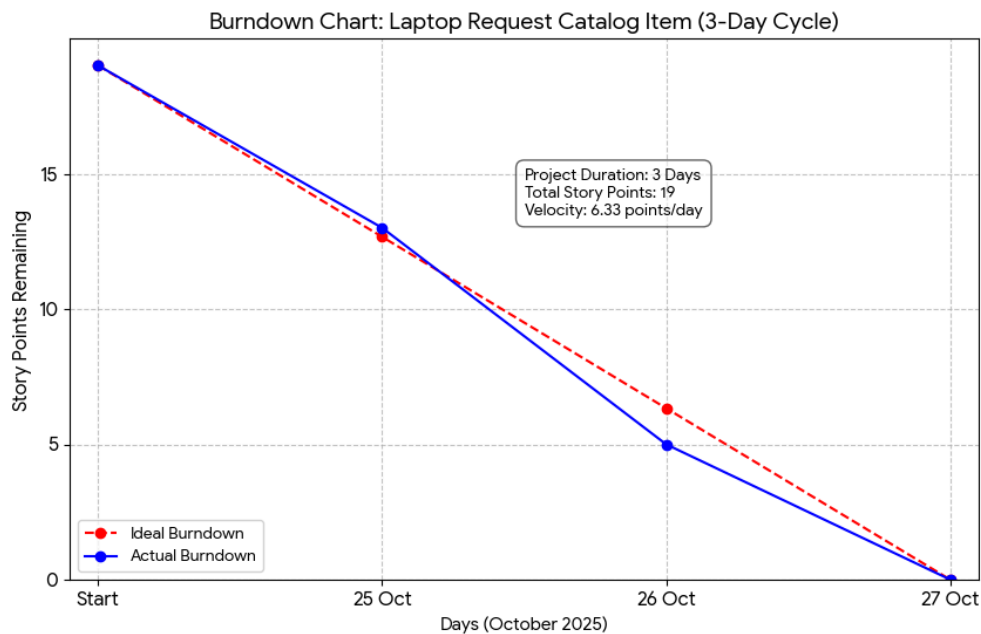

Burndown Chart Creation Process:

- **Ideal Burndown (Red Dashed Line):** The line starts at 19 points on Oct 25 and must linearly decrease to 0 points by the project end date of Oct 27.
- **Ideal Daily Rate:** 19 points / 3 days $\approx$ 6.33 points/day.
- The line has a steeper slope, indicating the aggressive pace required, where the team must complete a substantial amount of work each day to meet the short deadline.
- **Actual Burndown (Blue Solid Line):** This line reflects the remaining work at the end of each day, based on your planned sprint completions (19 $\rightarrow$ 13 $\rightarrow$ 5 $\rightarrow$ 0 points).
- **Visual Interpretation:** The blue line must closely follow the steep ideal line. If the team falls behind on any given day, the gap between the blue and red lines will open significantly, which highlights the high risk associated with this short execution window.
- **Velocity: 6.33 points/day.** This high velocity demonstrates the aggressive nature of the plan.
